

**SF Bay Area IRWMP Coordinating Committee Meeting Summary
May 18, 2020
Conference Call Dial-in Only**

1. Roll Call – Appointed Functional Area Representatives Present

Water Supply- Water Quality	Wastewater- Recycled Water	Flood Protection- Stormwater	Watershed	Disadvantaged Communities
<ul style="list-style-type: none"> • Steve Ritchie, SFPUC, Chair • Mark Seedall, CCWD 	<ul style="list-style-type: none"> • Cheryl Munoz, City of Hayward, representing BACWA 	<ul style="list-style-type: none"> • Brian Mendenhall, Valley Water 	<ul style="list-style-type: none"> • Josh Bradt, SFEP • Brenda Buxton, SCC • Judy Kelly, NBWA 	

Others Present:

Brad Arnold, Valley Water
 Y'anad Burrell, EBMUD
 Tess Byler, San Francisquito Creek JPA
 Taylor Chang, SFPUC
 Maddie Duda, EJCW
 Natasha Dunn, SFEP
 Adam French, Amah Mutsun Land Trust
 Ryan Hirano, EJCW
 Darcie Luce, SFEP
 James Muller, SFEP
 Michelle Novotny, SFPUC
 Kelsi Oshiro, ACWD
 Leslie Perry, SFEP
 Jake Spaulding
 Alex Tavizon, CIEA
 Aston Tennefoss, DWR

2. Status of Prop 84 Rounds 1-4

For Round 1, Josh Bradt reported receiving the retention payment from DWR. He is making the final retention payments to the local project sponsors and to SFEP for admin costs.

Round 2, Natasha Dunn reported the status of a couple approved project completion reports. Project 10 Bayfront Canal/Atherton Channel is compiling documentation for a potential time extension to be

formally submitted to DWR, including an MOU demonstrating a commitment to the project. Project 18 Upper York Creek is advertising their bid package.

For Round 3, James Muller reported all quarterly submittals are being reviewed and will be submitted to DWR. The submittals total about \$200,000. The round will likely be extended to the end of the year to allow time for final reporting for the last 3 or 4 projects.

For Round 4, Mr. Muller reported that Project 3 MMWD AMI had a sizable increase in construction implementation and are now at 66% complete. Project 6 San Francisquito Creek Flood Damage Reduction had their final project report approved by DWR. Project 7 Mountain View Shoreline and Project 8 Eden Landing will likely be amended in June or July.

Jake Spaulding provided an AQPI update. The San Francisco and East Bay X-Band radars are expected to be installed in the fall. There was a site visit to the East Bay radar site last Monday. Currently there is a users group meeting happening.

3. Status of Prop 1 IRWM DACTIP

SFEP submitted a progress report to DWR documenting all activities through the end of April. Currently, there isn't a South Bay outreach partner. The work on the homeless communities needs assessment is on hold due to COVID-19. The Pacific Institute is the program's technical advisor for homeless communities needs assessment.

Last Tuesday, there was a virtual meeting with many of the large Bay Area water providers and community members to discuss the scope for the regional tap water quality testing effort. The next step will be to have community meetings, continue discussions with the technical advisor at UCLA Luskin Center and the water agencies to further define the scope of what will be tested and where. Steve Ritchie commented that historically there has been a lot of focus on rural water quality issues, but the same attention hasn't been given to urban issues. We may want to explore this with the state and others in terms of whether this kind of effort could take place in other urban areas in California.

Ryan Hirano and Maddie Duda asked CC members if they know of other funding opportunities to help the outreach partners with some issues identified in the needs assessments that aren't directly related to the DACTIP.

Alex Tavizon reported on the Tribal outreach update. The regional tap water quality meeting was a great opportunity for Tribes to participate. 3 Tribes participated. CIEA has been working with DWR to facilitate and bring tribes to the Tribal Regional Water Management webinar series. The webinar series will be held on Tuesdays for the next 3 weeks at 8:50am-12pm. There was another Tribal Advisory Committee meeting where technical assistance needs including mapping were discussed.

The DACTIP Technical Advisory Committee (TAC) will be meeting after the CC meeting to delve into the tap water quality testing effort as well as potential changes to the format of the TAC meetings to ensure they are as meaningful as possible.

4. Discussion and Approval of CC Governance Structure Changes

The governance structure formalizes participation in the Coordinating Committee as outlined in the BAIRWMP. The governance structure relates to voting members, but it doesn't guarantee funding. The proposal is to add DACs and Tribes to the governance structure in order to give them a formal vote at the Coordinating Committee.

Michelle Novotny has been having discussions about tying the governance structure to funding allocations. The Plan includes the funding allocation guidelines we adopted for Prop 84 wherein the plan was to split funding equally by sub-region. There was the intention to also try to allocate funding fairly to each functional area. Ms. Novotny proposed the question of revisiting the funding allocation rules in the Plan. There was comment that the governance shouldn't be tied to funding allocation. There was another comment that funding allocations are target allocations, not requirements. There was another comment to see how process goes in dealing with allocations for Prop 1 and then revisit this question next year. There was a suggestion to document the funding allocation process during the next funding round.

Action Items:

- Ms. Chang will add to the next Coordinating Committee meeting agenda the vote to approve the proposed changes to the CC governance structure.
- Ms. Novotny will provide language on how the Plan will be updated to reflect the changes for the next CC meeting.

5. Status of Prop 1 Implementation Funding

Local project sponsors that have projects being funded under Round 1 should continue to adopt the Plan. Final award is anticipated for June 1. Then SFEP will begin drafting local project sponsor funding agreements.

Mr. Muller discussed the draft letter included in the CC meeting packet. The goal is to let the State know there are concerns about the timing for Round 2. Due to COVID-19, there have been delays in the ability of communities to meet and continue to develop project proposals that are ready in time for Round 2.

KEY

Project entirely closed out except for ongoing Post-Performance Reports
 Project with significant concerns

Critical Milestone achieved since last meeting.

ABAG/DWR Grant Agreement #4600010575 - Round 2							Construction Status Breakdown			Funds (as of Q20)	
Quarterly Status: Invoice 29 executed by DWR, retention invoice routing fro Projects 1, 3, 8, 19 Payments: None Amendments: None Pending Site Visits: None Grant Term: December 31, 2020							Complete:	15	Total Grant: \$20,000,000		
							Underway:	2	Total Match: \$13,470,177.66		
							Sig. Concerns:	2	Grant Funds Spent: \$17,084,445.49 (85.4%)		
							Withdrawn:	1	Match Funds Documented: \$9,899,778.72 (73.4%)		

Project # and Title	Project Sponsor	Construction Implementation Status	Project Completion Site Visit Date	Engineer's Cert of Completion Rcvd (Y/N)	Submission Date for Final Invoice	Project Completion Report Status	Retention Requested (Y/N)	Retention Paid (Y/N)	Post-Performance Report # Submitted	Anticipated Date Retention Release Invoice Issued to DWR
01_Bay Area Regional Water Conservation & Education Program	Solano County Water Agency	100%	Mar-19	N/A	Submitted	Final Approved by DWR	Y	N	None to Date	Jul-20
02_East Bayshore Recycled Water Project Phase 1A (Emeryville)	EBMUD	Complete	Nov-16	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
03_Lagunitas Creek Watershed Sediment Reduction & Managments	Marin Municipal WD	Complete	Nov-17	Y	Submitted	Final Approved by DWR	Y	N	#2	Jul-20
04_Marin/Sonoma Conserving our Watersheds, Agricult BMPs	Marin RCD	100%	Nov-17	Y	Submitted	Approved by DWR	Y	Y	None to Date	Closed
05_Napa Milliken Creek Flood Damage Reduction & Fish Passage Barri	County of Napa	Complete	Feb-18	Y	Submitted	Approved by DWR	Y	Y	None to Date	Closed
06_5th St. East & McGill Road Recycled Water	Sonoma Valley Cnty San Dist.	Complete	Nov-17	Y	Submitted	Final Approved by DWR	Y	Y	None to Date	Closed
07_Oakland Sausal Creek Restoration	City of Oakland Pub. Wks.	Complete	Apr-17	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
08_Pescadero Water Supply & Sustainability	County of San Mateo	100%	Mar-19	Y	Submitted	Final Approved by DWR	Y	N	None to Date	Jul-20
09_Petaluma Flood Reduction, Water & Habitat Quality for Capri Cree	City of Petaluma	99%	Feb-18	Y	Jun-20	On hold for final invoice submittal	N	N	None to Date	Aug-20
10_Bayfront Canal/Atherton Channel Flood Improve & Habitat Restore	Redwood City	0%	None to Date	N	Oct-20	Draft #1 Oct 2020	N	N	None to Date	Dec-20
11_Regional Groundwater Storage & Recovery Phase 1A	SFPUC	Complete	Jun-17	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
12_Richmond Breuner Marsh Restoration	East Bay Regional Park Dist.	Complete	Apr-17	Y	Submitted	Final approved by DWR	Y	Y	#2	Closed
13_Infrastructure Upgrades for Water Supply & Quality	Roseview Heights Mutual Water	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn
14_SF Bay Climate Change Pilot Projects	SFEP & Oro Loma San Dist	Complete	Apr-17	Y	Submitted	Final Approved by DWR	Y	Y	None to Date	Closed
15_SF Airport Reclaimed Water Facility	SFO/City of San Francisco	98%	Summer 2020	Y	In review	Draft #1 in review	N	N	None to Date	Sep-20
16_San Jose Green Streets & Alleys Demonstration	City of San Jose	Complete	May-18	Y	Submitted	Final Approved by DWR	Y	Y	None to Date	Closed
17_San Pablo Rheem Creek Wetlands Restoration	Contra Costa Water Dist.	Complete	Apr-17	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
18_Upper York Creek Dam Removal & Ecosystem Restoration	City of St Helena	0%	None to Date	N	Oct-20	Draft #1 Oct 2020	N	N	None to Date	Dec-20
19_Students & Teachers Restoring a Watershed (North & East Bays)	Point Blue Conservation	Complete	Feb-18	N/A	Submitted	Final Approved by DWR	Y	N	None to Date	Jul-20
20_Grant Administration	ABAG	N/A	N/A	N/A	Oct-20	Draft August 2020	N	N	N/A	Dec-20

ABAG/DWR Grant Agreement #4600010883 - Round 3 (Drought Round)							Construction Status Breakdown			Funds (as of Q17)	
Quarterly Status: Invoice 28 (Q18) materials were uploaded to DWR at the end of May. Q19 materials will be due at the end of July. Payments: Payment for Invoice 25 (Q17) was received 6/11/2020. Payments to LPS's were sent out mid June. Amendments: SFEP is currently working on finalizing the SFPUC and MMWD LPS amendments. SFEP will submit a Grant Agreement amendment request to extend the grant in June. Site Visits: None this period Grant Term: September 30, 2020 - will be extended to December 31, 2020							Complete:	6	Total Grant: \$32,178,423		
							Underway:	4 (all over 60%)	Total Match: \$25,121,180.72		
							Sig. Concerns:	0	Grant Funds Spent: \$31,680,428.84 (98%)		
							Withdrawn:	0	Match Funds Documented: \$25,121,180.72 (100%)		

Project # and Title	Project Sponsor	Construction Implementation Status	Project Completion Site Visit Date	Engineer's Cert of Completion Rcvd (Y/N)	Submission Date for Final Invoice	Project Completion Report Status	Retention Requested (Y/N)	Retention Paid (Y/N)	Post-Performance Report # Submitted	Anticipated Date Retention Release Invoice Issued to DWR
01_Lower Cherry Aqueduct Emergency Rehabilitation	SFPUC	95%	Oct-19	Y	Submitted	draft #1 Spring 2020	N	N	None to Date	Jul-20
02_Zone 7 Water Supply Drought Preparedness	Zone 7	Complete	Aug-16	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
03_Los Carneros Water Dist. & Milliken Sarco-Tulocay Recycled Water	Napa Sanitation District	Complete	Aug-16	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
04_Sunnyvale Continuous Recycled Water Production & Wolfe Rd Pipe	Santa Clara Valley WD	100%	May-18	N	Submitted	Draft #1 Winter 2019	N	N	None to Date	Mar-20
05_DERWA Phase 3 Recycled Water Expansion	DSRSanDist/EBMUD	Complete	May-16	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
06_Callistoga Recycled Water Storage Facility	City of Callistoga	Complete	Aug-16	Y	Submitted	Final Approved by DWR	Y	Y	#3	Closed
07_Drought Relief for South Coast San Mateo County	San Mateo RCD	99%	Jun-17	N	May-20	Draft #1 Spring 2020	N	N	None to Date	Sep-20
08_Stinson Beach Water Supply & Drought Preparedness	Stinson Beach County WD	Complete	Mar-19	Sep-18	Submitted	Final Approved by DWR	Y	Y	#1	Closed
09_Bay Area Regional Drought Relief Conservation Program	StopWaste	100%	Mar-19	N/A	Submitted	Final Approved by DWR	Y	Y	None to Date	Closed
10_WaterSMART Irrigation with AMI/AMR	Marin Municipal WD	90%	Mar-19	N/A	Jun-20	Draft #1 Summer 2020	N	N	None to Date	Jun-20
11_Grant Administration	ABAG	N/A	N/A	N/A	Sep-20	Draft #1 Fall 2020	N	N	N/A	Dec-20

ABAG/DWR Grant Agreement #4600011486 - Round 4

Quarterly Status: Invoice 24 (Q15) submittals were uploaded to DWR at the end of May. Q16 materials are due to ABAG at the end of July.

Payments: Payment for Q15 expected by the end of August.

Amendments: SFEP will move forward with amending the Grant Agreement for SMRCD as DWR has requested that we wait June/July to amend projects 07 and 08 to assess progress

Site Visits: None occurred this reporting period

Grant Term: December 31, 2020

Construction Status Breakdown

Complete: 2
 Underway: 3
 Sig. Concerns: 2
 Withdrawn: 1


Funds (as of Q14)

Total Grant: \$21,469,025
 Total Match: \$22,395,709
 Grant Funds Spent: \$8,601,771.72 (40%)
 Match Funds Documented: \$12,747,949 (55.6%)

Project # and Title	Project Sponsor	Construction Implementation Status	Project Completion Site Visit Date	Engineer's Cert of Completion Rcvd (Y/N)	Submission Date for Final Invoice	Project Completion Report Status	Retention Requested (Y/N)	Retention Paid (Y/N)	Post-Performance Report # Submitted	Anticipated Date Retention Release Invoice Issued to DWR
01_Grant Administration	ABAG	N/A	N/A	N/A	Jun-21	Dec-20	N	N	N/A	Aug-21
02_Anderson Dam Seismic Retrofit	Santa Clara Valley WD	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn	Withdrawn
03_Marin 2020 AMI Phase II	Marin Municipal WD	66%	None to Date	N/A	Sep-20	Draft #1 September 2020	N	N	None to Date	Aug-20
04_East Palo Alto Groundwater Supply	City of East Palo Alto	100%	Aug-18	Jul-18	Jun-20	Draft #1 August 2020	N	N	None to Date	Dec-20
05_Coastal San Mateo County Drought Relief Phase II	San Mateo RCD	95%	None to Date	Apr-19	Feb-20	Draft #1 July 2020	N	N	None to Date	Aug-20
06_SFQuito Creek Flood Damage Reduction & Ecosystem Restore Phase 2	SFQuito Creek JPA	100%	Dec-19	May-19	Submitted	Final Approved by DWR	Y	N	None to Date	Jun-20
07_Mt View Shoreline Portion of SBSPR	State Coastal Conservancy	0%	None to Date	N			N	N	None to Date	
08_Eden Landing Portion of SBSRPR	State Coastal Conservancy	0%	None to Date	N			N	N	None to Date	
09_Novato Creek Flood Protection and Habitat Enhancement	State Coastal Conservancy	10%	None to Date	Sep-21	Dec-21	Draft #1 December 2020	N	N	None to Date	Dec-20

**Bay Area IRWMP
Functional Area Representation**

Name	Functional Area	Agency	Functional Area Body
Steve Ritchie	Chair/Water supply-Water quality	SFPUC	
Lisa Bankosh	Vice-chair	SCVWD	
Brian Mendenhall	Flood protection-Stormwater	SCVWD	BAFPAA
Mark Boucher	Flood protection-Stormwater	CCCFCWCD	BAFPAA
Carol Mahoney	Flood protection-Stormwater	Zone 7	BAFPAA
Cheryl Munoz	Wastewater- Recycled water	City of Hayward	BACWA
Florence Wedington	Wastewater- Recycled water	EBMUD	BACWA
Mark Seedall	Water supply-Water quality	CCWD	BAWAC
Brad Sherwood	Water supply-Water quality	SCWA	BAWAC
Brenda Buxton	Watershed	State Coastal Conservancy	BAWN
Judy Kelly	Watershed	NBWA	BAWN
Josh Bradt	Watershed	SFEP	BAWN

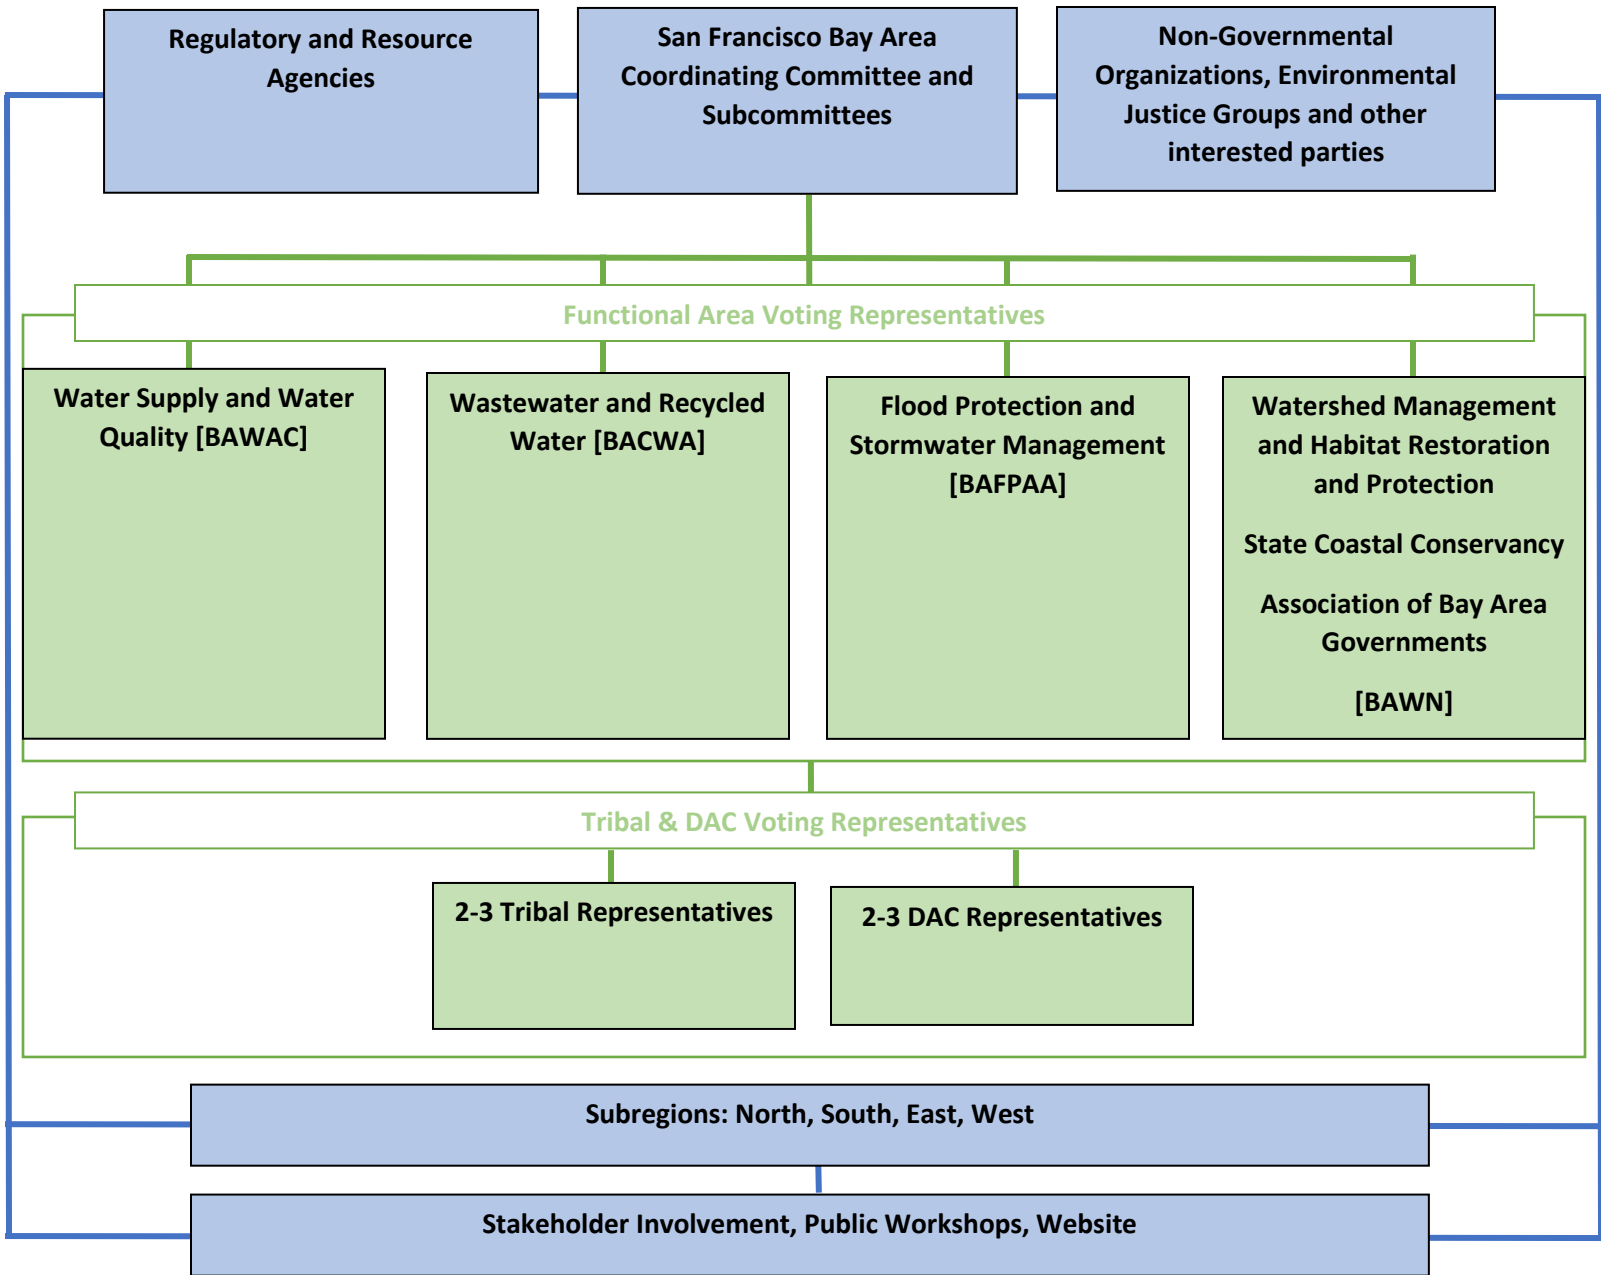

IRWM Sections on Governance Structure and Voting

<p>Section 1.2.4: “The four FAs are represented in the CC by three designated individuals, or their alternates, and are considered the “voting representatives.” Voting representatives are appointed by their respective FA groups and may change over time. If the CC is not able to reach consensus on an item that needs a decision, the Chair or Vice Chair may ask for a vote from this body. However, this situation has yet to arise and the group has been successful in achieving consensus in all cases.”</p>	<p>Details how Functional Areas are represented and how a vote is called.</p>
<p>Section 1.2.5: “Calculations of area and population within each Subregion were used to establish ‘Target Allocations’ for funding. Areas and population were weighted as follows:</p> <p>50% distribution based on number of Subregions (4)</p> <p>25% distribution based on population in each Subregion</p> <p>25% distributed based on area of each Subregion</p> <p>Based on these calculations the following allocation targets were established:</p> <p>North Bay 25%</p> <p>East Bay 29%</p> <p>South Bay 25%</p> <p>West Bay 22%”</p>	<p>Target allocations were established for Subregions, but not for FAs. In Section 6.4.2, the 2019 PSC philosophy for scoring did not consider these target allocations and instead sought a more equal distribution of the funding.</p>
<p>Appendix A-2 Voting Principles</p>	<p>The Voting Principles do not state any particular voting rules (i.e. $\frac{2}{3}$ vs simple majority), but does note that tie votes result in a non-vote during any particular vote and that Chair/Vice-Chair do not have tie-breaking privilege. Minimum</p>

	quorum of one voting representative or alternate member from each Functional Area is required for any vote. The addition of Disadvantaged Communities and Tribal representatives would not alter anything in the CC Voting Principles.
Section 6.4.2	This section explains the scoring philosophy and results from the 2019 PSC. There was relatively equal distribution of projects across subregions and FAs.



Final Awards List – Round 1 Integrated Regional Water Management (IRWM) Implementation Grant Solicitation

Disclaimer: The Final Award is estimated and conditional until final terms and conditions are agreed upon and an agreement has been executed. The awarded grant amount listed in the executed agreement can be less than the Final Award amount listed here based upon final negotiations between the Awardee and DWR. An "Award Notification Letter" will be mailed shortly to the successful applicants (awardees) listing the conditions that must be met before DWR will enter into a Grant Agreement with the awardee and additional requirements that must be addressed to maintain eligibility to receive grant funds.

Funding Area: San Francisco Bay Area							
IRWM Region: San Francisco Bay Area		Applicant: Association of Bay Area Governments					
Project Name	Project Implementing Agency	Implementing Agency Type	Primary Benefit	DAC Implementation Funds		General Implementation Funds	
				Requested	Awarded	Requested	Awarded
Grant Agreement Administration	Association Of Bay Area Governments	Public Agency				\$994,550	\$994,550
Calistoga Water and Habitat Project	Napa County Resource Conservation District	Public Agency	Water Supply Reliability			\$2,028,808	\$2,028,808
Upstream San Francisquito Creek Flood Protection, Ecosystem Restoration, and Recreation Project	San Francisquito Creek Joint Powers Authority	Public Agency	Flood Protection			\$2,964,479	\$2,964,479
Bay Area Water Conservation	East Bay Municipal Utilities District (+10 Others)	Public Utility	Water Conservation			\$4,177,875	\$4,177,875
San Francisco Zoo Recycled Water Pipeline Project	San Francisco Public Utilities Commission	Public Utility	Water Supply - Recycled Water			\$538,051	\$538,051
RD1 System Fish Passage Improvements	Alameda County Water District	Public Agency	Fishery Improvements			\$3,346,992	\$3,346,992
North Bay Water Reuse Project Phase II	City of American Canyon, City of Petaluma	Public Agency	Water Supply - Recycled Water			\$4,061,270	\$4,061,270
River Oaks Stormwater Capture	City of San Jose - Public Works Department	Public Agency	Stormwater Management			\$3,203,550	\$3,203,550
Lower Walnut Creek Restoration	Contra Costa County Flood Control and Water Conservation District	Public Agency	Ecosystem Restoration			\$1,434,425	\$1,434,425
Totals:				\$0	\$0	\$22,750,000	\$22,750,000
				Total DAC Implementation Award:	\$0	Total General Implementation Award:	\$22,750,000
Total Final Award						\$22,750,000	

DEPARTMENT OF WATER RESOURCES

1416 NINTH STREET, P.O. BOX 942836
SACRAMENTO, CA 94236-0001
(916) 653-5791



June 9, 2020

James Muller
Principal Environmental Planner
Association of Bay Area Governments
375 Beale Street, Suite 700
San Francisco, CA 94105

Award Notification for Round 1 Proposition 1 Integrated Regional Water Management (IRWM) Implementation Grant, San Francisco Bay Area Funding Area

Dear Mr. Muller:

Congratulations! We are pleased to inform you that the proposal, San Francisco Bay Area IRWM: Building Resilience for Sustainable Communities, filed by Association of Bay Area Governments has been awarded **\$22,750,000** by the Department of Water Resources (DWR) for the Round 1 Proposition 1 IRWM Implementation Grant Solicitation. Costs incurred after June 2, 2020 will be eligible for grant reimbursement and costs incurred after January 1, 2015 can be used as required local cost share. This award is conditioned upon the execution of a Grant Agreement between DWR and your agency. Please see the [Agreement Template](#) for your reference.

Your timely attention is directed to the following requirements:

Within 14 calendar days of the date of this award letter:

Award Acceptance - Please submit a letter or e-mail signed by the authorized representative (agreement signatory) confirming your agency as the Grantee to accept the grant award in the amount of \$22,750,000 and your commitment to provide the required non-State cost share of 50% of the total project costs, excluding projects receiving a cost share waiver or reduction.

Electronic Signatures - DWR uses DocuSign to process signatures electronically to expedite all grant-related documents requiring a signature. In order for DWR to send documents to you via DocuSign, we need your permission and consent. If you consent to the use of DocuSign, please send DWR a letter on official letterhead signed by the authorized representative, consenting to the use of DocuSign for all transactions related to this award. Please contact the DWR Project Manager if you would like sample language. If you prefer not to use electronic signatures, DWR can send documents for original (wet) signatures via email or mail, but this can delay the process significantly, especially during situations such as the COVID-19 public health emergency.

Within 60 calendar days of the date of this award letter, or as otherwise specified in the attachment:

Eligibility Requirements - Attachment 1 (Eligibility Criteria Self Certification Form) outlines the conditions that must be met before the grant agreement can be executed and additional requirements that must be addressed to maintain continuing eligibility and receive grant funds. Please complete, sign (electronically if possible) and submit the form and any required additional documentation to the DWR Project Manager according to the specified time periods.

Mr. Muller
June 9, 2020
Page 2

Changes to Work Plan, Budget, and/or Schedule: Please submit a list of projects to be included in the Grant Agreement and any changes to the work plan, budget, and/or schedule since the proposal was submitted. Any proposed changes should be submitted as a Word document in track changes to the original document (work plan, budget and/or schedule), and an explanation of the changes provided. Changes will only be considered acceptable by DWR if the project maintains or increases the level of quality and benefits as compared to the original proposal, unless the grant award amount is less than what was requested in the proposal.

Following receipt of all required information, the DWR Project Manager will work with you to complete the grant agreement for execution and schedule a kick-off meeting.

Your timely attention to these requirements is critical to execute the Grant Agreement; failure to do so may result in DWR revoking the grant award. Please submit the required information in the time periods specified to the DWR Project Manager Aston Tennefoss at Aston.Tennefoss@water.ca.gov.

Please contact Maria Lorenzo-Lee at Maria.Lorenzo-Lee@water.ca.gov or (916) 657-4893 or Desiree Ramirez at Desiree.Ramirez@water.ca.gov or (916) 653-0975 for any questions regarding the required materials.

Again, congratulations to you and your Local Project Sponsors on this well-deserved grant award. Our team appreciates the time and effort you contributed to this new and improved grant solicitation process and we will be reaching out in coming months to get your feedback for use in developing the process for Round 2 starting in 2021. We look forward to working with you to complete these IRWM projects to build water resilience in your communities.

Sincerely,

Carmel Brown

Carmel Brown P.E.

Chief, Financial Assistance Branch

Division of Regional Assistance

ML BE

Attachment 1 – Eligibility Criteria Self-Certification Form

BAIRWMP Coordinating Committee
Schedule of Future CC Meetings

Date	Location
July 27, 2020	Virtual?
August 24, 2020	Virtual?
September 28, 2020	Virtual?
